



আন্তর্জাতিক ইসলামী বিশ্ববিদ্যালয় চট্টগ্রাম
الجامعة الإسلامية العالمية شيتاغونغ
International Islamic University Chittagong

Kumira, Chattogram-4318, Bangladesh.

Tel : 03042 51154-61, Ext: 366, Fax : 03042 51160, E-mail : info@iiuc.ac.bd
www.iiuc.ac.bd

Ref.:

Date :

২২ অক্টোবর ২০২২ইং


সম্মানিত সরবরাহকারী,
আসসালামু আলাইকুম ওয়ারাহমাতুল্লাহ।

আন্তর্জাতিক ইসলামী বিশ্ববিদ্যালয় চট্টগ্রামের আইটি বিভাগের অফিস ও ডাটাসেন্টার লেভেল-৫ থেকে লেভেল-২ এ স্থানান্তরের জন্য জেনুইন আইটি ফার্মের কাছে দরপত্র আহ্বান করা হচ্ছে। আপনার দরপত্রটি আগামীকাল ২৫ অক্টোবর ২০২২ইং তারিখের মধ্যে নিম্নোক্ত ই-মেইলে/ সরাসরি পাঠানোর জন্য অনুরোধ করা হল।

বিশেষ দৃষ্টব্য:

- প্রতিটি পার্টসের ওয়ারেন্টি, স্পেসিফিকেশন, ব্রান্ড (প্রযোজ্য ক্ষেত্রে) ইত্যাদি স্পষ্টভাবে উল্লেখ করতে হবে।
- ভ্যাট ও টেক্স সরকারী বিধি অনুযায়ী কর্তন করা হবে।
- খুবই দ্রুত সময়ের মধ্যে কাজটি সম্পন্ন করার প্রস্তুতি থাকতে হবে।
- কাজের বিস্তারিত সিডিউল এতদসঙ্গে সংযুক্ত করা হল।
- কোটেশন পাঠানোর ই-মেইল ঠিকানাঃ mmhppdiuc@gmail.com, faisalahamed2002@yahoo.com & jafurulh@yahoo.com
- সিডিউল সম্পর্কিত বিষয়ে বিস্তারিত জানতে কল করুনঃ 01832251669 (ইঞ্জিনিয়ার ফয়সাল আহমদ, নেটওয়ার্ক এডমিনিস্ট্রেটর, আইটিডি)/01814-130112 (জনাব মুহাম্মদ জাফরুল হক, আইটি অফিসার, আইটিডি)

নিবেদক-


০২.১০.২০২২

মুহাম্মদ ফয়সাল

পরিচালক,

পারচেজ এন্ড প্রকিউরমেন্ট ডিভিশন, আইআইইউসি।

Date:

Schedule A

“Raised Floor for the Datacenter at IIUC Kumira”

1. Floor space/area:21' X 13'


2. Specification Details:

SL	Component	Brand	Description	Qty	Price	Remarks
01	Solid Panel	ZT/AT/	HPL Decorated Panel Breadth Size : 600mm x 600mm Panel Thickness : 35mm Concentrated load : ≥ 3600 N Uniform Load(N/m ²) : 12000 Ultimate Uniform Load : 36000 N Systematically anti-static Fire-proof Damp proof foam concrete filled panels Support heavy load, easy to install, disassembly. Difficult to be dirty, easy to clean, decorative. Appearance and durable using term. Standard : MOB (BRITAIN), CISCA (USA)/ equivalent ISO 9001, ISO 14001 * CE Certified			
02	Perforated Panel	ZT/AT/	HPL Decorated Panel Breadth Size : 600mm x 600mm Panel Thickness : 35mm Concentrated load : ≥ 3600 N Uniform Load(N/m ²) : 12000 Ultimate Uniform Load : 36000 N Ultimate Load : 10800 N Flatness : ≤ 5 mm Finished Floor Height : up to FFH 300mm Systematically anti-static Fire-proof Damp proof foam concrete filled panels Support heavy load, easy to install, disassembly and interchange Difficult to be dirty, easy to clean, decorative. Appearance and durable using term. Standard : MOB (BRITAIN), CISCA (USA)/equivalent ISO 9001, ISO 14001 * CE Certified			
03	Pedestal	ZT/AT/	FLAT HEAD PEDESTAL	01		
04	Stringer	ZT/AT/	STRINGER AND SCREWS	01		
05	Panel Lifter		Panel Lifter Double Cup, Weight lifting capability 48 Kg.	01		
06	Floor Insulation		Thermal Insulation with top side antistatic foil paper pasting for heat preservation Key Specifications for Thermal Insulation:-Thickness: 18 mm Key Specifications for Foil Paper:-Thickness: 0.08mm- Liner: Silver release paper			
07	Installation, Detection Testing, Commissioning			01		

22/10/2022
Prof. Dr. Mohammed Humayun Kabir
Treasurer
National Islamic University Chittagong

Dr. Md. Shamimul Haque Choudhury
Chairman
ITD Management Committee
Int'l Islamic University Chittagong
Director (In-charge)
Information Technology Division
Int'l Islamic University Chittagong

3. Layout:

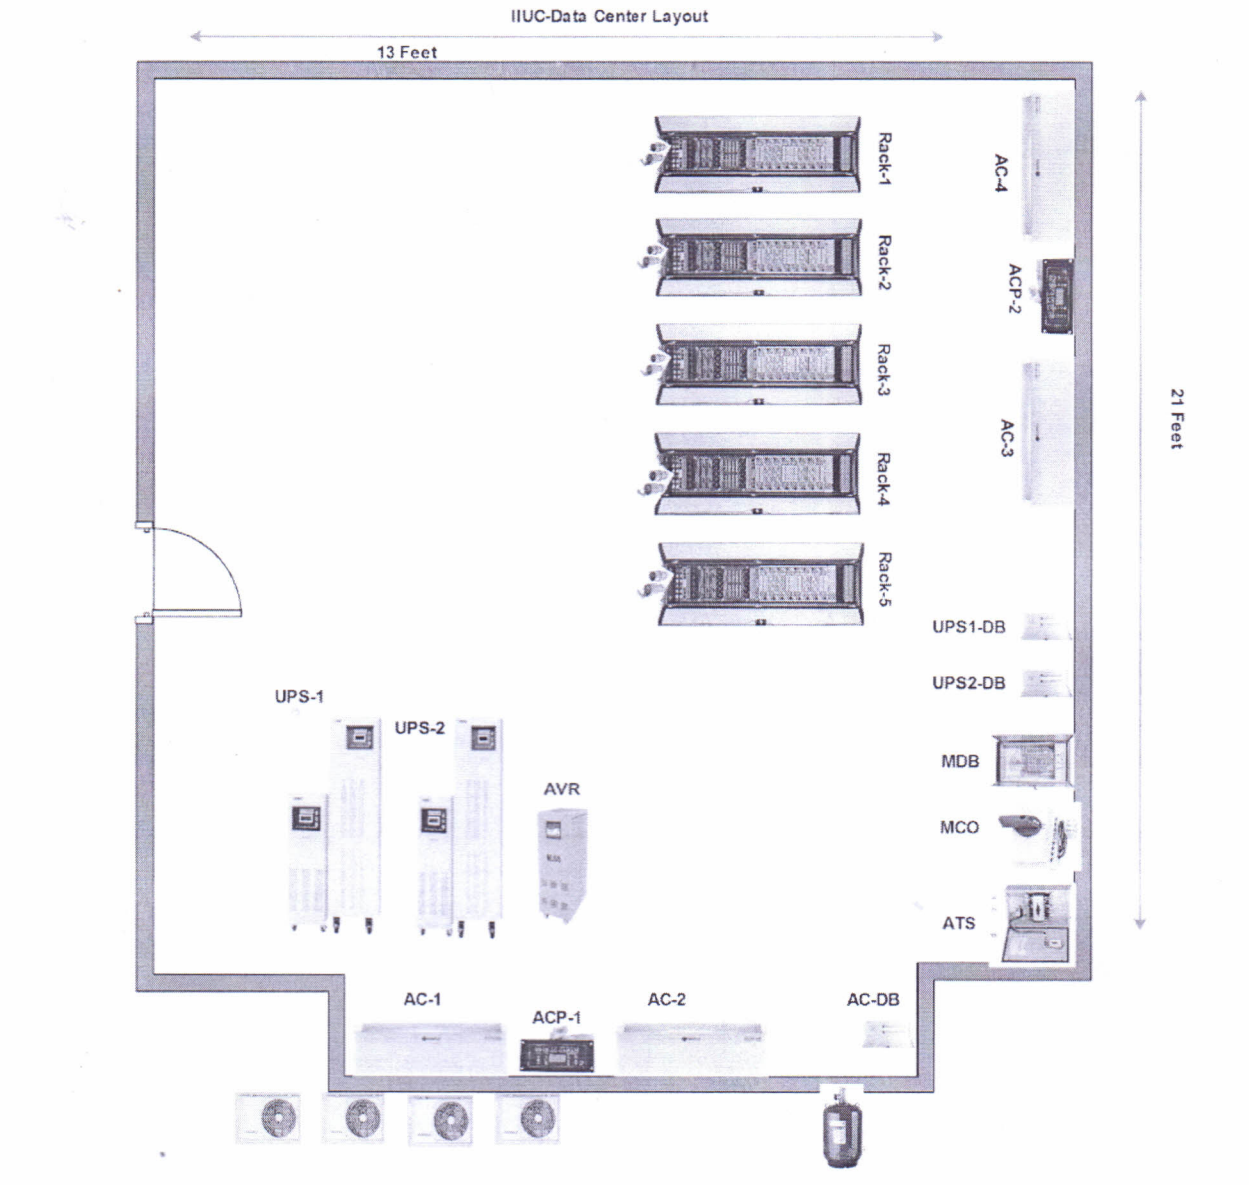

[Signature]
Dr. Md. Shamimul Haque Choudhury
Chairman
TD Management Committee
Islamic University Chittagong


[Signature]
Director (In-charge)
Information Technology Division
International Islamic University Chittagong


[Signature]
22.10.22
Prof. Dr. Mohammed Humayun Kabir
Treasurer
International Islamic University Chittagong

Schedule B

"Power Systems of the Datacenter at IIUC Kumira"

1. Proposed Layout:

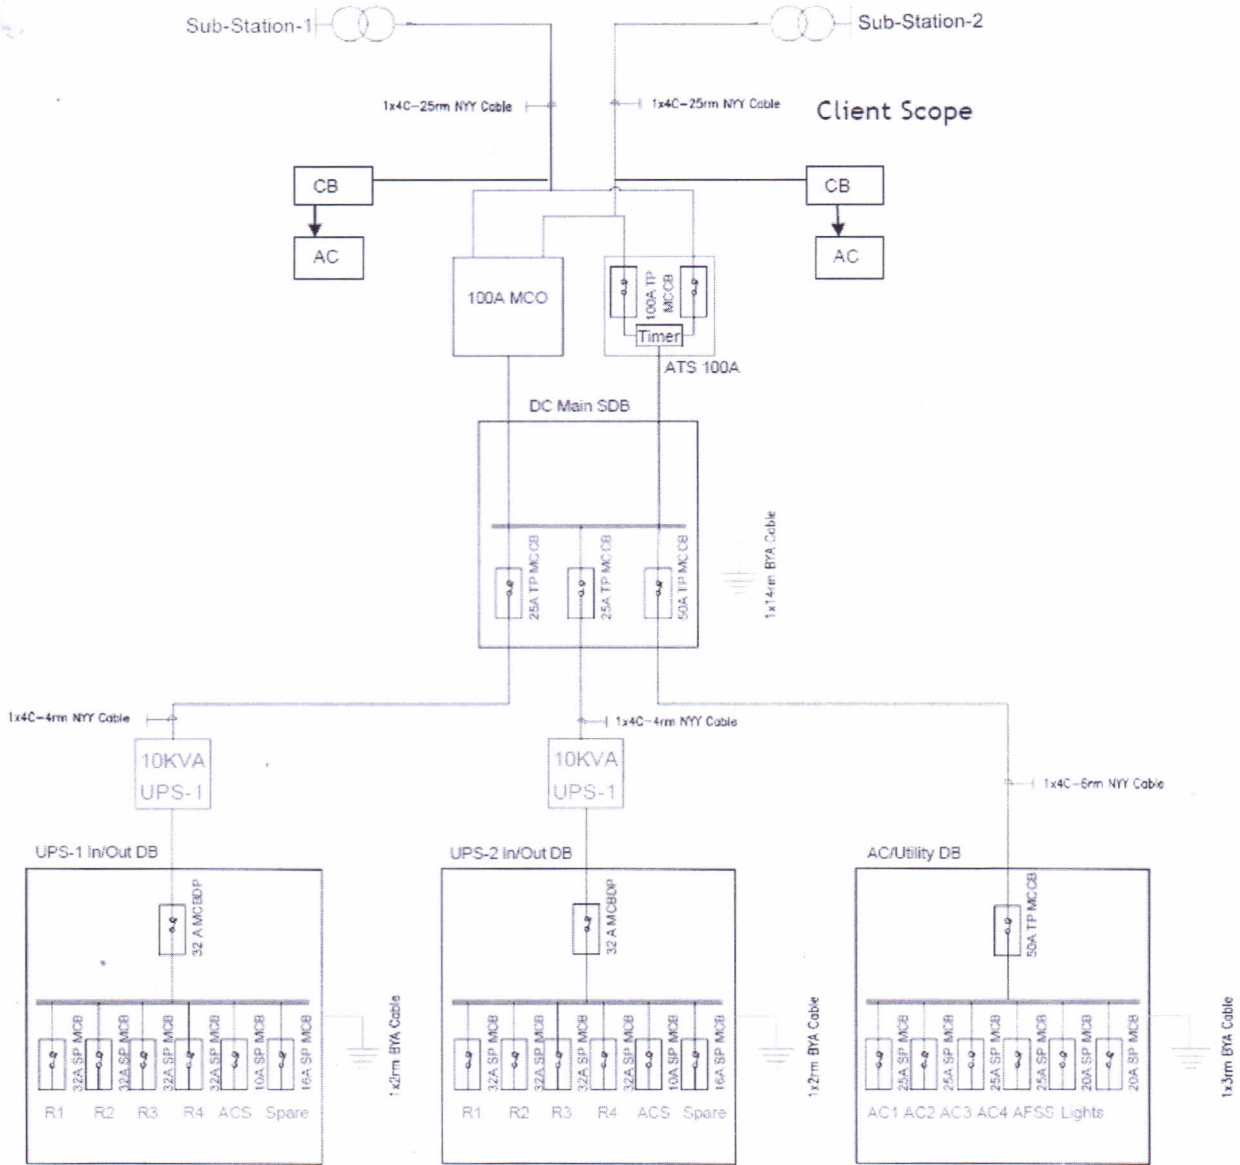



 22.10.2022
Prof. Dr. Mohammed Humayun Kabir
 Treasurer
 International Islamic University Chittagong


Dr. Md. Shamimul Haque Choudhury
 Chairman
 ITD Management Committee
 Int'l Islamic University Chittago...g


Director (In-charge)
 Information Technology Division
 Int'l Islamic University Chittagong.

2. Required power components/accessories for electrical/power system works of the Data Center:

SL	Component	Brand	Description	Qty	Unit Price	Total Price
01	ATS (100A) (automatic changeover Switch)	Fuji-Japan or ABB- German	WithCircuit Breaker, Magnetic contactor etc.	01		
02	MCO (100A) (Manual changeover Switch)			01		
03	MDB/ (Server room Sub Distribution Board)	Do	ABB/Schneider-Korea.	01		
04	Timer for AC	Do		02		
05	DB for UPS	Do		01		
06	DB for AC	Do		01		
07	UPS Mini DB	Do		01		
08	Rack mount Grounding Bar			As Required		
09	Industrial Socket Male-Female		3-phase+N	As Required		
10	Combined Socket	MK- Singapur		"		
11	Cables & others	BRB/ Eastern		"		
12	PVC Pipe	RFL		"		
13	Flexible Pipe	RFL		"		
14	MK Box white	RFL		"		
15	Installation with Accessories					


 22.10.2022
 Prof. Dr. Mohammed Humayun Kabir
 Treasurer
 International Islamic University Chittagong



 Dr. Md. Shamimul Haque Choudhury
 Chairman
 ITD Management Committee
 Int'l Islamic University Chittagong

 Director (In-charge)
 Information Technology Division
 International Islamic University Chittagong

Schedule C

“Automatic Fire Suppression System for the Datacenter at IIUC Kumira”

SL	Item	Description	Unit	Qty	Unit Price	Total Price
01	Automatic Fire Suppression System	<p>Suppression Agent (Gas) FM200 Model: HFC 227ea (FM200) Brand: Sanjing or Novec-1230 (FK-5-1-12)Fluid Agent Model: Novec-1230 (FK-5-1-12) Brand:3M;</p> <p>Suppression Agent quantity/ Cylinder Suppression Agent Capacity/Nozzle/etc. should be as per requirement of the Datacenter space/area (21'x13')</p>				
02	Detection system	<p>4 Detection and 2 Extinguishing Area Control Panel with Gas release and with (minimum) 4 SLA Batteries for control panel, Flashing Light, Evacuate Sign, Gas Discharge Sign, Alarm Bell, Auto Exit Sign, Manual Release or Break Glass, Photo Electric Heat Detector (atleast 4), Photo Electric Smoke Detector (at least 4), Caution Sign, etc.</p> <p>should be as per requirement of the Datacenter of space/area (21'x13')</p>				
03	Mechanical fitting & Electrical fitting	as per requirement				
05	Installation	Installation, Testing, Commissioning with line leak test & flow test	job	01		


 22.10.2022
Prof. Dr. Mohammed Humayun Kabir
 Treasurer
 International Islamic University Chittagong


Dr. Md. Shamimul Haque Choudhury
 Chairman
 ITD Management Committee
 Int'l Islamic University Chittagong


Director (In-charge)
 Information Technology Division
 Int'l Islamic University Chittagong.
